

# HEIGHT SAFETY INSPECTION REPORT

**Inspection No. 2214**

Client

**DeMartini Fletcher Property**  
Level 10, 46 Edward Street Brisbane QLD 4000

Site

**Site No. 2419**  
Anglicare - 12 King Street, Caboolture

Client Contact

**Clare Burton**  
0732112033  
[Maintenance@demartini.com.au](mailto:Maintenance@demartini.com.au)

Reviewed By: Damien Hewitt (Supervisor)  
Damien/supervisor

Safe@Heights  
Height Safety Specialists

18 Rowland St, Slacks Creek QLD 4127  
Phone: 07 3208 5833  
[sales@safeatheights.com.au](mailto:sales@safeatheights.com.au)  
[www.safeatheights.com.au](http://www.safeatheights.com.au)



## Table of Contents

Disclaimer .....	p. 3
The Complete Solution .....	p. 4
Proudly Queensland .....	p. 5
Inspection Scope .....	p. 6
Roof Plan .....	p. 8
MAIN ROOF - Item #1: Fold Down Ladder Certification .....	p. 9
Item #1: Fold Down Ladder Compliance Report .....	p. 11
MAIN ROOF - Item #2: Step Type Ladder Certification .....	p. 14
Item #2: Step Type Ladder Compliance Report .....	p. 16
MAIN ROOF - Item #3: Hatch Certification .....	p. 19
Item #3: Hatch Compliance Report .....	p. 20
MAIN ROOF - Item #4: Walkway Certification .....	p. 22
Item #4: Walkway Compliance Report .....	p. 23
MAIN ROOF - Item #5: Observation .....	p. 25
MAIN ROOF - Item #6: Observation .....	p. 27
MAIN ROOF - Item #7: Observation .....	p. 29



## DISCLAIMER

This Height Safety Report has been produced by Safe @ Heights Pty Ltd. It specifies the type/s and numbers of the height safety systems installed on this building. Only qualified and competent persons should use a height safety system and only after they have been authorised to do so by the system owner. All users must have undergone the correct training and be deemed competent to use the system/s.

A detailed Safe Work Method Statement (SWMS) must be completed prior to using any height safety system. A rescue plan must accompany all SWMS when using a fall arrest system. It is the responsibility of the owner of this system to ensure the following BEFORE the system can be safely used as per below:

- The design is fit for purpose
- There is an induction available that clearly explains how to use the system/s safely and that all works undergo this prior to using the system/s
- The user/s has the required training, experience and PPE to use the system safely
- All workers comply with current safety procedures as stated in the current Codes of Practice and Australian Standards for working at heights
- Use of a Full Body Harness with Energy Absorber complying with AS/NZ 1891.1 must be used when connected to any fall arrest system

Safe @ Heights Pty Ltd does not take any responsibility for or are liable for any injury or death caused by incorrectly using this system/a or any other system which has been installed or certified by Safe @ Heights Pty Ltd. Safe @ Heights Pty Ltd expressly prohibits the illegal use of this document. This document should be used as a guide only in the creation and planning of a specific SWMS and rescue plan by all users. Report is to be used exclusively for the purpose it was designed for, and is not to be copied, reproduced or distributed in any way in part or wholly without permission of Safe @ Heights Pty Ltd

**Height Safety is everyone's responsibility.**

**DO NOT USE THIS SYSTEM/S IF YOU DO NOT FEEL COMPETENT TO USE THE SYSTEM  
CORRECTLY AND SAFELY.**

# THE COMPLETE SOLUTION

## Who we are

Safe@Heights specialise in fall prevention, fall arrest and height access solutions. Whether your requirement is as simple as a ladder bracket to access a roof, a complete building solution or a state wide project, we can help. Our projects range in size from \$1000 to over \$500,000. As a Queensland based manufacturer and installer there is nothing we can't do.

The benefits of dealing directly with the manufacturer who also completes the installations are;

- High quality Queensland made products
- Custom solutions specifically designed for your site
- Specialist knowledge that only comes from thousands of hours of designing and testing height safety systems
- Longer Product and Installation Warranties
- Installation by highly trained trade qualified installers
- Your own dedicated Project Manager
- Access to OH&S specialists
- Peace of mind that you have the right solution for you





## PROUDLY QUEENSLAND



### QLD MADE

As the manufacturer and installer there is nothing we can't do. Over 95% of our systems have been proudly designed, engineered and manufactured right here in Queensland. Safe@Heights specialises in fall prevention, fall arrest and access solutions. Regardless of your requirements we are able to help you. Whether it is as simple as a ladder bracket to access a roof, a complete building solution or a state wide project, we can help. Our projects range in size from \$1000 to over \$500,000. As the manufacturer we are able to provide customised solutions that suit your unique requirements and budget.



### TRADE QUALIFIED

Our installers are all trade qualified and extensively trained in height safety system installation. We do not use subcontractors. All installations, servicing, inspections and certifications are completed by our own dedicated team. They know our products inside and out. Compliance and safety is guaranteed. Our team of installers are proud of our Queensland Made Systems and take the utmost care and attention with our installations. Close enough is never good enough for our team. They are perfectionists who love what they do.



### INSPECTIONS & AUDITS

All height safety access, fall prevention and fall arrest systems must be inspected and certified as compliant and safe on a regular basis. This is not only to ensure you are complying with your legal duties under the Work Health and Safety Act and Australian Standards, but more importantly to ensure that your systems are safe to use and remain fit for purpose

To assist you with this, we have our Certification & Safety Program. We take all the hassle and worry out of inspecting, certifying and maintaining your systems. Members enjoy a number of benefits such as our industry leading 15 Year Warranty\*, automatic inspection scheduling and free access to our HawkPro Compliance Management System.

For more information about becoming a member please contact our team at any time on (07) 3208 5733.



### QUALITY ASSURANCE

All of our installations come with a standard 5 Year Product and Installation Warranty. Members of our Certification & Safety Program automatically get upgraded to our Industry Leading 15 Year Warranty on all of our HawkPro systems. For any non HawkPro systems, the manufacturers product warranty will apply. However, the installation warranty is extended to 15 Years. Please refer to our warranty policy for full terms and conditions.

# HEIGHT SAFETY INSPECTION REPORT

## Inspection - Anglicare - 12 King Street, Caboolture

Safe@Heights has completed an inspection of the above address.

Please see below a summary of the systems inspected, followed by individual system certificates and full audit report. Where an item has failed or an issue has been identified, it will be highlighted red. Please take the time to review the report in full, including any of our recommendations. If you have any questions, please do not hesitate to contact us at any time.

Your next inspection due date is listed in the below table. We will be in contact with you approximately 6 weeks prior to this date to arrange the next service.

Thank you for partnering with Safe@Heights to maintain your height safety system compliance. If we can be of further service please do not hesitate to contact us.

## Important Information

Warning: This roof has multiple noncompliant and high risk issues. We recommend a full audit

## Summary Table

Job #	2214
Site Contact	Kai Kapusta - 0435 947 675
Date of Inspection	11/04/2025
Date of Next Inspection	11/04/2026
Certified By	Damien Hewitt (Supervisor), Aaron Parr

## Height Safety Systems Summary Table

System Type	Quantity
Fold Down Ladder - Amboss AM BOSS - Fold Down Ladder	1
Step Type Ladder - Unknown/Not Marked Step Type Ladder	1
Hatch - Unknown/Not Marked Hatch	1
Walkway - Steel Walkway	1

## Failed Items and Recommendations

System Type	Item Status	Recommendation
-------------	-------------	----------------

# HEIGHT SAFETY INSPECTION REPORT

MAIN ROOF - Item #1 - Fold Down Ladder - FDL1	PWC	Warning: Fold Down Ladder has Passed With Conditions (PWC) and approved for limited use. The non-compliances identified include: Minimal foot clearance between ladder rungs and the lid surface with also a smaller top step which may affect footing and stability when transitioning to the next ladder. Be sure to maintain 3 points of contact at all times when using the system. We recommend that the ladder is replaced to improve safety and reduce overall risk
MAIN ROOF - Item #2 - Step Type Ladder - STL1	PWC	Warning: Step Type Ladder has Passed With Conditions (PWC) and has minor non-compliance with AS1657. The first step is smaller than standard - potentially impacting foot stability, and the system is positioned between a fold down ladder and hatch - requiring careful transition. System should only be used by trained personnel, maintain 3 points of contact at all times and take extra caution when stepping on/off the first rung. Access onto the roof does not comply with AS1657. See next item
MAIN ROOF - Item #3 - Hatch - HT1	PWC	The hatch is compliant, however it does not have three sides of guard railing as per requirement of AS1657:2018. We recommend the installation of a hatch guard rail safety system
MAIN ROOF - Item #5 - Observation - OBS1 - No Height Safety Systems	High Risk - Identified hazard	Warning: This roof area is not equipped with compliant fall protection systems. Access to this roof should be limited until appropriate safety controls are installed and certified by a competent person
MAIN ROOF - Item #6 - Observation - OBS2 - Plant deck Guardrail	Medium Risk - Identified hazard	Warning: This plant deck does not have compliant edge protection or guardrails, creating a fall hazard in breach of AS1657.2018
MAIN ROOF - Item #7 - Observation - OBS3 - No Access onto Roof / Rusted Roof Sheets/Fall Hazards	High Risk - Identified hazard	Warning: DO NOT ENTER this lower roof area. Roof sheets have been identified as severely rusted and structurally compromised. This area is non-compliant without safe access and structural requirements under AS1657 and must not be accessed under any circumstances. Access should be prohibited until the roof is repaired and certified safe by a competent person. At the same time, fall prevention systems should be considered for accessing plant or having the plant removed and installed in a safe location



## Roof Plan

### Roof Plan



### Elevations





### MAIN ROOF - Item #1: Fold Down Ladder Certification

<b>Inspection Date</b>	11/04/2025	<b>Job Number</b>	1339
<b>Company Name</b>	DeMartini Fletcher Property	<b>Site Address</b>	Anglicare - 12 King Street, Caboolture
<b>Contact Name</b>	Clare Burton	<b>Site Contact Name</b>	
<b>Contact Phone</b>		<b>Site Contact Phone</b>	
<b>Identification #:</b>	FDL1		
<b>Type of System:</b>	FOLD DOWN LADDER		
<b>Brand/Model</b>	Amboss AM BOSS - Fold Down Ladder		
<b>System Location:</b>	MAIN ROOF		
<b>Date of Installation:</b>	Unknown		
<b>Date of Next Service:</b>	11/04/2026		
<b>Technician:</b>	SAFE @ HEIGHTS PTY LTD (Damien Hewitt (Supervisor), Aaron Parr)		
<b>Status:</b>	<b>PWC</b>		
<b>PWC Condition:</b>	Minor noncompliance/Low risk. Additional care required during use/access. Prior to use/access person/s must be provided with this report and understand the issue. Only authorised person/s can access		
<b>PWC Details:</b>	125mm foot clearance from front of ladder rung to the Fold Down Ladder lid Top step is 210mm from top of ladder rung to top of Fold Down Ladder User to be aware when climbing the lader		
<b>Recommendations:</b>	Warning: Fold Down Ladder has Passed With Conditions (PWC) and approved for limited use. The non-compliances identified include: Minimal foot clearance between ladder rungs and the lid surface with also a smaller top step which may affect footing and stability when transitioning to the next ladder. Be sure to maintain 3 points of contact at all times when using the system. We recommend that the ladder is replaced to improve safety and reduce overall risk		
<b>Client Notes</b>	Warning: Fold Down Ladder has Passed With Conditions (PWC) and approved for limited use. The non-compliances identified include: Minimal foot clearance between ladder rungs and the lid surface with also a smaller top step which may affect footing and stability when transitioning to the next ladder. Be sure to maintain 3 points of contact at all times when using the system. We recommend that the ladder is replaced to improve safety and reduce overall risk		

SAFE @ HEIGHTS PTY LTD CERTIFIES THAT THE ABOVE LISTED SYSTEMS HAVE BEEN INSPECTED IN ACCORDANCE WITH MANUFACTURERS INSTRUCTIONS AND RELEVANT AUSTRALIAN STANDARDS. THIS INSPECTION DOES NOT INCLUDE THE ROOF STRUCTURE.

**WARNING:** It is the responsibility of the owner of this system to ensure the following BEFORE the system can be safely used:

- The design is fit for purpose.
- A detailed SWMS has been written after a risk assessment of the site has been completed.
- Only persons who have the necessary competence should use this system.
- Authorisation to access this area must be obtained from the owner.
- All safety procedures must be complied with as stated in the current safety codes of practice for working at heights.

SAFE @ HEIGHTS PTY LTD IS NOT RESPONSIBLE FOR, NOR LIABLE FOR THE MISUSE OF THIS SYSTEM

### Item #1: Fold Down Ladder Compliance Report

Identification #	FDL1
Date of Certification	11/04/2025
Date of Next Certification	11/04/2026
Date Installed	Unknown
Who installed this system?	
Brand/Model	Amboss AM BOSS - Fold Down Ladder

1 Example Photo







2 Type of fold down ladder	Other
2.1 Other	
3 What is the vertical height from ceiling to floor?	3000mm
4 What is the width of the ladder between the stiles?	465mm
5 What angle in degrees is the ladder when extended?	69°
6 What is the width of the ladder rungs?	80mm
7 How is the ladder installed?	Fixed into solid frame
7.3 Take a photo and describe how it has been fixed to the frame and if there are any issues	
<b>Notes:</b> Tek screws into steel frame	



Has the system Passed/Failed?	PWC
<b>PWC Condition:</b>	Minor noncompliance/Low risk. Additional care required during use/access. Prior to use/access person/s must be provided with this report and understand the issue. Only authorised person/s can access
<b>PWC Details:</b>	125mm foot clearance from front of ladder rung to the Fold Down Ladder lid Top step is 210mm from top of ladder rung to top of Fold Down Ladder User to be aware when climbing the ladder
<b>Recommendations:</b>	Warning: Fold Down Ladder has Passed With Conditions (PWC) and approved for limited use. The non-compliances identified include: Minimal foot clearance between ladder rungs and the lid surface with also a smaller top step which may affect footing and stability when transitioning to the next ladder. Be sure to maintain 3 points of contact at all times when using the system. We recommend that the ladder is replaced to improve safety and reduce overall risk

### MAIN ROOF - Item #2: Step Type Ladder Certification

<b>Inspection Date</b>	11/04/2025	<b>Job Number</b>	1339
<b>Company Name</b>	DeMartini Fletcher Property	<b>Site Address</b>	Anglicare - 12 King Street, Caboolture
<b>Contact Name</b>	Clare Burton	<b>Site Contact Name</b>	
<b>Contact Phone</b>		<b>Site Contact Phone</b>	
<b>Identification #:</b>	STL1		
<b>Type of System:</b>	STEP TYPE LADDER		
<b>Brand/Model</b>	Unknown/Not Marked Step Type Ladder		
<b>System Location:</b>	MAIN ROOF		
<b>Date of Installation:</b>	Unknown		
<b>Date of Next Service:</b>	11/04/2026		
<b>Technician:</b>	SAFE @ HEIGHTS PTY LTD (Damien Hewitt (Supervisor), Aaron Parr)		
<b>Status:</b>	<b>PWC</b>		
<b>PWC Condition:</b>	Minor noncompliance/Low risk. Additional care required during use/access. Prior to use/access person/s must be provided with this report and understand the issue. Only authorised person/s can access		
<b>PWC Details:</b>	Bottom rung is 150mm from steel beam - cut to size to fit in cavity between Fold Down Ladder and Hatch lid		
<b>Recommendations:</b>	Warning: Step Type Ladder has Passed With Conditions (PWC) and has minor non-compliance with AS1657. The first step is smaller than standard - potentially impacting foot stability, and the system is positioned between a fold down ladder and hatch - requiring careful transition. System should only be used by trained personnel, maintain 3 points of contact at all times and take extra caution when stepping on/off the first rung. Access onto the roof does not comply with AS1657. See next item		
<b>Client Notes</b>	Warning: Step Type Ladder has Passed With Conditions (PWC) and has minor non-compliance with AS1657. The first step is smaller than standard - potentially impacting foot stability, and the system is positioned between a fold down ladder and hatch - requiring careful transition. System should only be used by trained personnel, maintain 3 points of contact at all times and take extra caution when stepping on/off the first rung. Access onto the roof does not comply with AS1657. See next item		

SAFE @ HEIGHTS PTY LTD CERTIFIES THAT THE ABOVE LISTED SYSTEMS HAVE BEEN INSPECTED IN ACCORDANCE WITH MANUFACTURERS INSTRUCTIONS AND RELEVANT AUSTRALIAN STANDARDS. THIS INSPECTION DOES NOT INCLUDE THE ROOF STRUCTURE.

**WARNING:** It is the responsibility of the owner of this system to ensure the following BEFORE the system can be safely used:

- The design is fit for purpose.
- A detailed SWMS has been written after a risk assessment of the site has been completed.
- Only persons who have the necessary competence should use this system.
- Authorisation to access this area must be obtained from the owner.



- All safety procedures must be complied with as stated in the current safety codes of practice for working at heights.

*SAFE @ HEIGHTS PTY LTD IS NOT RESPONSIBLE FOR, NOR LIABLE FOR THE MISUSE OF THIS SYSTEM*


## Item #2: Step Type Ladder Compliance Report

Identification #	STL1
Date of Certification	11/04/2025
Date of Next Certification	11/04/2026
Date Installed	Unknown
Who installed this system?	
Brand/Model	Unknown/Not Marked Step Type Ladder
1 Example Photo	



2 What is the ladder made from?	Aluminium
3 Vertical height of ladder from top platform to bottom platform. (Must not exceed 6000mm)	1550mm
4 Bottom Platform	Does not require bottom platform
4.1 On concrete base or mesh base which has cross level & inline level under 7°	
4.1.1 Cross Level (degrees)	0°
4.1.2 Inline level (degrees)	0°

<b>5</b> Excluding the bottom tread, are all the treads no less than 200mm and no more than 300mm and the same space apart, within $\pm 5$ mm?	Yes
<b>5.1</b> Tread Spacings (mm)	235mm
<b>5.2</b> Height from top of bottom platform to top of first tread (mm). Must be within 10% of tread spacing.	150mm
<b>5.3</b> Warning: Ladder has failed.	

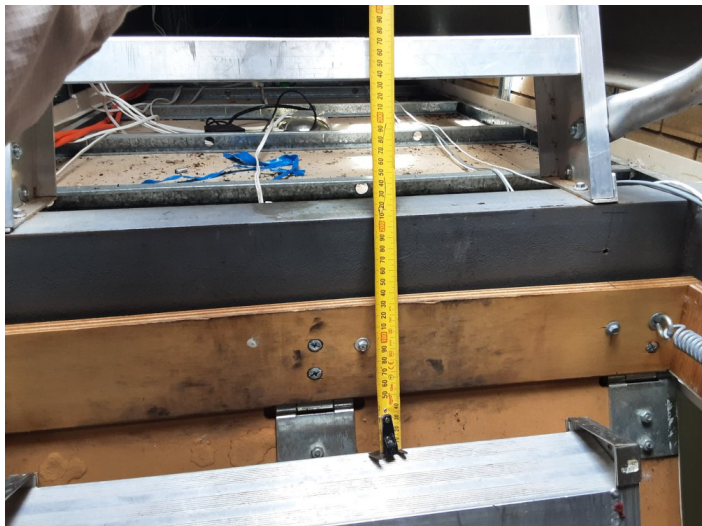

<b>6</b> The tread width must not be less than 100mm. Tread width:	100mm
<b>7</b> Do the treads have a knurled or anti-slip surface?	Yes
<b>8</b> Is there a minimum distance of 200mm for each tread, measured from the front edge back, to any object?	Yes
<b>9</b> Is the top tread level with the top platform?	Yes
<b>10</b> What is the distance between the inside of the stiles of the main ladder body? Must be between 450mm and 750mm	510mm
<b>11</b> The hand railing must be between 150mm and 200mm from the ladder stile. Actual measurement is:	160mm
<b>12</b> The hand railing must start no more than 900mm from the ground. The current hand railing measurement is:	50mm
<b>13</b> Does the hand railing extend up and onto the platform?	Yes
<b>14</b> The inside distance between the hand railings must not be less than 550mm and greater than 750mm. The actual inside measurement is:	600mm
<b>15</b> Is there clear hand space of 50mm around the stiles?	Yes
<b>16</b> Top Platform	Does not require top platform
<b>16.1</b> On concrete base or mesh base which has cross level & inline level under 3°	
<b>16.1.1</b> Cross Level (degrees)	3°
<b>16.1.2</b> Inline level (degrees)	0°
<b>17</b> Step type ladders should be between 60° and 70°. Actual angle is:	66°



<b>18</b> Are all the fixings in good condition?	Yes
<b>19</b> Does the ladder have a:	NA
<b>20</b> Is there anything else that needs to be addressed?	Yes
<b>20.1</b> Describe the issues and take photos where applicable	
<b>Notes:</b> Access onto the roof does not comply	



Has the system Passed/Failed?	PWC
<b>PWC Condition:</b>	Minor noncompliance/Low risk. Additional care required during use/access. Prior to use/access person/s must be provided with this report and understand the issue. Only authorised person/s can access
<b>PWC Details:</b>	Bottom rung is 150mm from steel beam - cut to size to fit in cavity between Fold Down Ladder and Hatch lid
<b>Recommendations:</b>	Warning: Step Type Ladder has Passed With Conditions (PWC) and has minor non-compliance with AS1657. The first step is smaller than standard - potentially impacting foot stability, and the system is positioned between a fold down ladder and hatch - requiring careful transition. System should only be used by trained personnel, maintain 3 points of contact at all times and take extra caution when stepping on/off the first rung. Access onto the roof does not comply with AS1657. See next item

### MAIN ROOF - Item #3: Hatch Certification

<b>Inspection Date</b>	11/04/2025	<b>Job Number</b>	1339
<b>Company Name</b>	DeMartini Fletcher Property	<b>Site Address</b>	Anglicare - 12 King Street, Caboolture
<b>Contact Name</b>	Clare Burton	<b>Site Contact Name</b>	
<b>Contact Phone</b>		<b>Site Contact Phone</b>	
<b>Identification #:</b>	HT1		
<b>Type of System:</b>	HATCH		
<b>Brand/Model</b>	Unknown/Not Marked Hatch		
<b>System Location:</b>	MAIN ROOF		
<b>Date of Installation:</b>	Unknown		
<b>Date of Next Service:</b>	11/04/2026		
<b>Technician:</b>	SAFE @ HEIGHTS PTY LTD (Damien Hewitt (Supervisor), Aaron Parr)		
<b>Status:</b>	<b>PWC</b>		
<b>PWC Condition:</b>	Part of Area/System has failed. Failed items/area cannot be used/accessed safely. Refer to report. Recommend no access until rectified and made safe. If use/access is required additional controls must be implemented and documented in SWMS prior to use/access. Do not use/access without authorisation and approval of the additional controls from PCBU and recorded in your SWMS		
<b>Recommendations:</b>	The hatch is compliant, however it does not have three sides of guard railing as per requirement of AS1657:2018. We recommend the installation of a hatch guard rail safety system		
<b>Client Notes</b>	The hatch is compliant, however it does not have three sides of guard railing as per requirement of AS1657:2018. We recommend the installation of a hatch guard rail safety system		

SAFE @ HEIGHTS PTY LTD CERTIFIES THAT THE ABOVE LISTED SYSTEMS HAVE BEEN INSPECTED IN ACCORDANCE WITH MANUFACTURERS INSTRUCTIONS AND RELEVANT AUSTRALIAN STANDARDS. THIS INSPECTION DOES NOT INCLUDE THE ROOF STRUCTURE.

**WARNING:** It is the responsibility of the owner of this system to ensure the following BEFORE the system can be safely used:

- The design is fit for purpose.
- A detailed SWMS has been written after a risk assessment of the site has been completed.
- Only persons who have the necessary competence should use this system.
- Authorisation to access this area must be obtained from the owner.
- All safety procedures must be complied with as stated in the current safety codes of practice for working at heights.

**SAFE @ HEIGHTS PTY LTD IS NOT RESPONSIBLE FOR, NOR LIABLE FOR THE MISUSE OF THIS SYSTEM**

### Item #3: Hatch Compliance Report

Identification #	HT1
Date of Certification	11/04/2025
Date of Next Certification	11/04/2026
Date Installed	Unknown
Who installed this system?	
Brand/Model	Unknown/Not Marked Hatch

#### 1 Example Photo



2 What system leads to the hatch?	Step Type Ladder
3 What type of hatch is installed?	Standard Access Hatch
4 What are the opening measurements?	

Length (mm): 1450mm		Width (mm): 840mm	
5 Does the hatch have gas struts to help it open?		Yes	
5.1 Are they in good working condition?		Yes	
6 Is the opening size sufficient to allow a minimum of 750mm from front of ladder access rung to back edge of hatch? Record measurement in mm		1230mm	
7 How do you step out of the hatch?		Directly Forward	
<b>Has the system Passed/Failed?</b>	<b>PWC</b>		
<b>PWC Condition:</b>	Part of Area/System has failed. Failed items/area cannot be used/accessed safely. Refer to report. Recommend no access until rectified and made safe. If use/access is required additional controls must be implemented and documented in SWMS prior to use/access. Do not use/access without authorisation and approval of the additional controls from PCBU and recorded in your SWMS		
<b>Recommendations:</b>	The hatch is compliant, however it does not have three sides of guard railing as per requirement of AS1657:2018. We recommend the installation of a hatch guard rail safety system		



### MAIN ROOF - Item #4: Walkway Certification

<b>Inspection Date</b>	11/04/2025	<b>Job Number</b>	1339
<b>Company Name</b>	DeMartini Fletcher Property	<b>Site Address</b>	Anglicare - 12 King Street, Caboolture
<b>Contact Name</b>	Clare Burton	<b>Site Contact Name</b>	
<b>Contact Phone</b>		<b>Site Contact Phone</b>	
<b>Identification #:</b>	WW1		
<b>Type of System:</b>	WALKWAY		
<b>Brand/Model</b>	Steel Walkway		
<b>System Location:</b>	MAIN ROOF		
<b>Date of Installation:</b>	Unknown		
<b>Date of Next Service:</b>	11/04/2026		
<b>Technician:</b>	SAFE @ HEIGHTS PTY LTD (Damien Hewitt (Supervisor), Aaron Parr)		
<b>Status:</b>	<b>PASS</b>		
<b>Recommendations:</b>	The hatch is compliant, however it does not have three sides of guard railing as per requirement of AS1657:2018. We recommend the installation of a hatch guard rail safety system		
<b>Client Notes</b>			

SAFE @ HEIGHTS PTY LTD CERTIFIES THAT THE ABOVE LISTED SYSTEMS HAVE BEEN INSPECTED IN ACCORDANCE WITH MANUFACTURERS INSTRUCTIONS AND RELEVANT AUSTRALIAN STANDARDS. THIS INSPECTION DOES NOT INCLUDE THE ROOF STRUCTURE.

**WARNING:** It is the responsibility of the owner of this system to ensure the following BEFORE the system can be safely used:

- The design is fit for purpose.
- A detailed SWMS has been written after a risk assessment of the site has been completed.
- Only persons who have the necessary competence should use this system.
- Authorisation to access this area must be obtained from the owner.
- All safety procedures must be complied with as stated in the current safety codes of practice for working at heights.

*SAFE @ HEIGHTS PTY LTD IS NOT RESPONSIBLE FOR, NOR LIABLE FOR THE MISUSE OF THIS SYSTEM*


#### Item #4: Walkway Compliance Report

Identification #	WW1
Date of Certification	11/04/2025
Date of Next Certification	11/04/2026
Date Installed	Unknown
Who installed this system?	
Brand/Model	Steel Walkway

1 Example Photo



2 What is the walkway made from?	Steel
3 Type of surface it is mounted to	Trimdek
4 Take a photo of the roof profile	

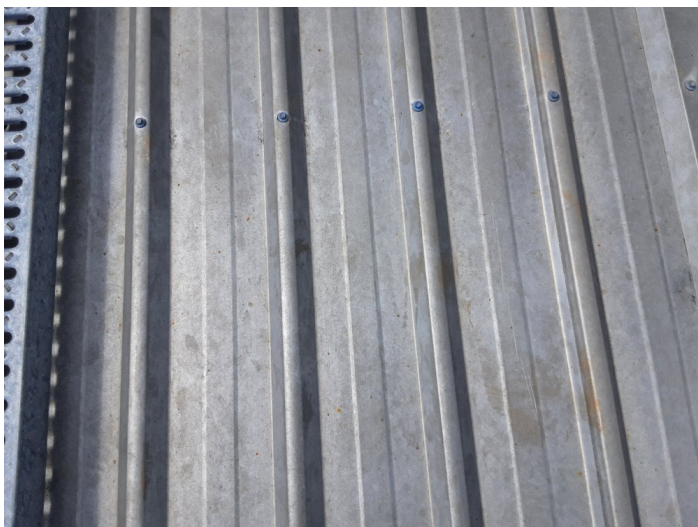

5 How long is the section of walkway in metres?	3m
6 Walkway must be a minimum of 600mm wide. The width of the walkway is:	670mm
7 What is the pitch of the roof in degrees?	5°
8 Does the walkway run across the roof pitch?	Yes
9 Does the walkway run up the roof pitch?	Yes
10 Are all the joiner and end bars correctly installed and with require fixings?	Yes
11 Are all the fixings in good condition and installed correctly?	Yes
12 Anything else needs to be noted?	No
Has the system Passed/Failed?	PASS

### MAIN ROOF - Item #5: Observation

Identification #	OBS1 - No Height Safety Systems
Date of Observation	01/07/2025
1 Name of Observation	No Height Safety Systems
2 Take a photo of the observation	



Photo taken from building next door - no systems installed



Photo taken from building next door - no systems installed



Photo taken from building next door - no systems installed

3 Describe the issue with as much detail as required	No height Safety systems on roof. May need anchors installed if work is to be done on the gutters
Observation Status:	High Risk - Identified hazard




**Recommendations:**

Warning: This roof area is not equipped with compliant fall protection systems. Access to this roof should be limited until appropriate safety controls are installed and certified by a competent person

## MAIN ROOF - Item #6: Observation

Identification #	OBS2 - Plant deck Guardrail
Date of Observation	01/07/2025
1 Name of Observation	Plant deck Guardrail
2 Take a photo of the observation	

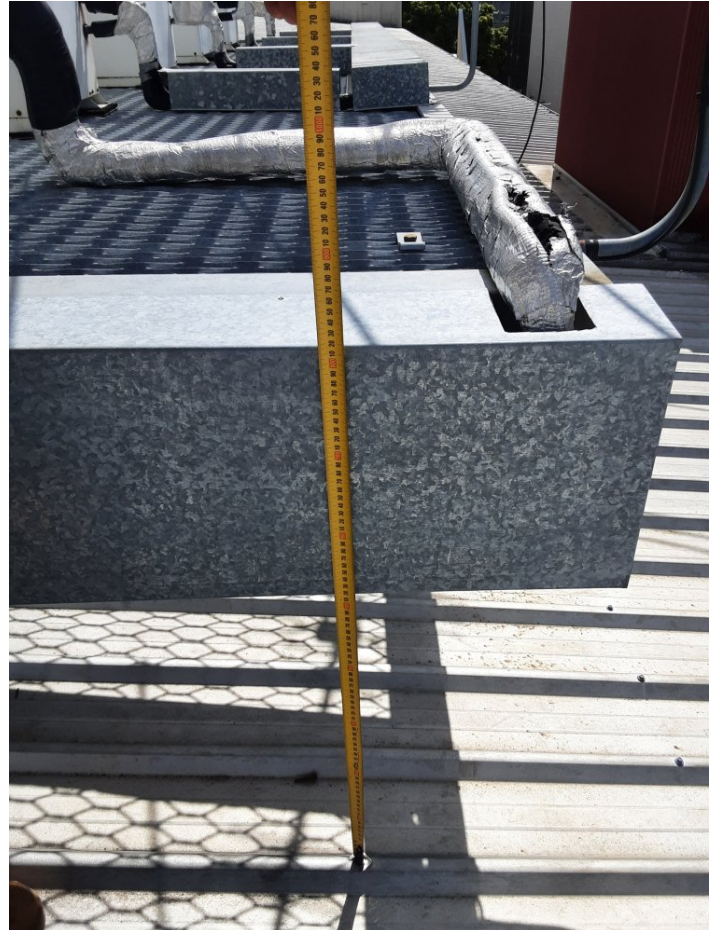

815mm drop off of plantdeck onto roof



75x200 c beam

### 3 Describe the issue with as much detail as required

Plant deck is over 300mm in height with no guard railing. AS1657 states where a platform is over 300mm guard railing must be installed. It would require 26m of side mount guardrail to go around plant deck. There are a number of aircon units on the plant deck.  
The plant deck has a 75mm x 200mm c beam a 10mm thick around the perimeter.

#### Observation Status:

Medium Risk - Identified hazard

#### Recommendations:

Warning: This plant deck does not have compliant edge protection or guardrails, creating a fall hazard in breach of AS1657.2018




## MAIN ROOF - Item #7: Observation

Identification #	OBS3 - No Access onto Roof / Rusted Roof Sheets/Fall Hazards
Date of Observation	01/07/2025
1 Name of Observation	No Access onto Roof / Rusted Roof Sheets
2 Take a photo of the observation	



580mm parapet wall




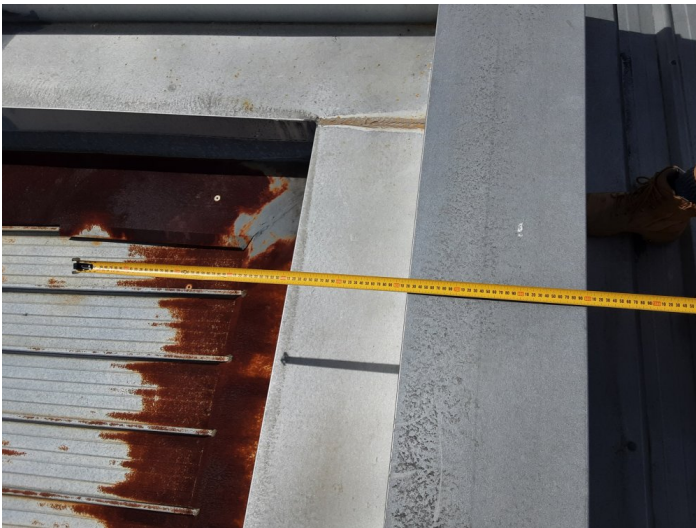

980mm crossover



1200mm walkway space

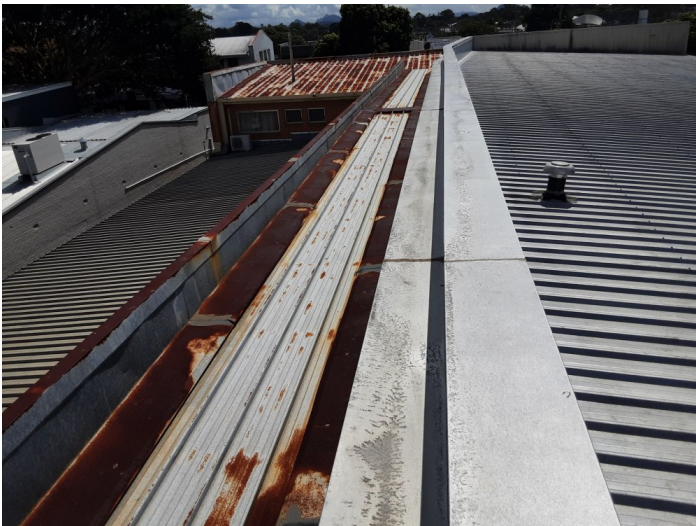

1200mm walkway space





**3** Describe the issue with as much detail as required

<b>Observation Status:</b>	High Risk - Identified hazard
<b>Recommendations:</b>	Warning: DO NOT ENTER this lower roof area. Roof sheets have been identified as severely rusted and structurally compromised. This area is non-compliant without safe access and structural requirements under AS1657 and must not be accessed under any circumstances. Access should be prohibited until the roof is repaired and certified safe by a competent person. At the same time, fall prevention systems should be considered for accessing plant or having the plant removed and installed in a safe location
